


# Weekly Progress Report

5-11-2026 through 5-15-2026

Work Location: Crummer South (Los Angeles County)

APN: 2069-078-906

Overview: The goats continue to clear brush in section CS 01. A total of 4 acres were cleared this week, progress has slowed down due to denser vegetation. The denser vegetation has pushed the new estimated start date for grazing in the area of Big Rock Malibu to the week of 5/25/2026.

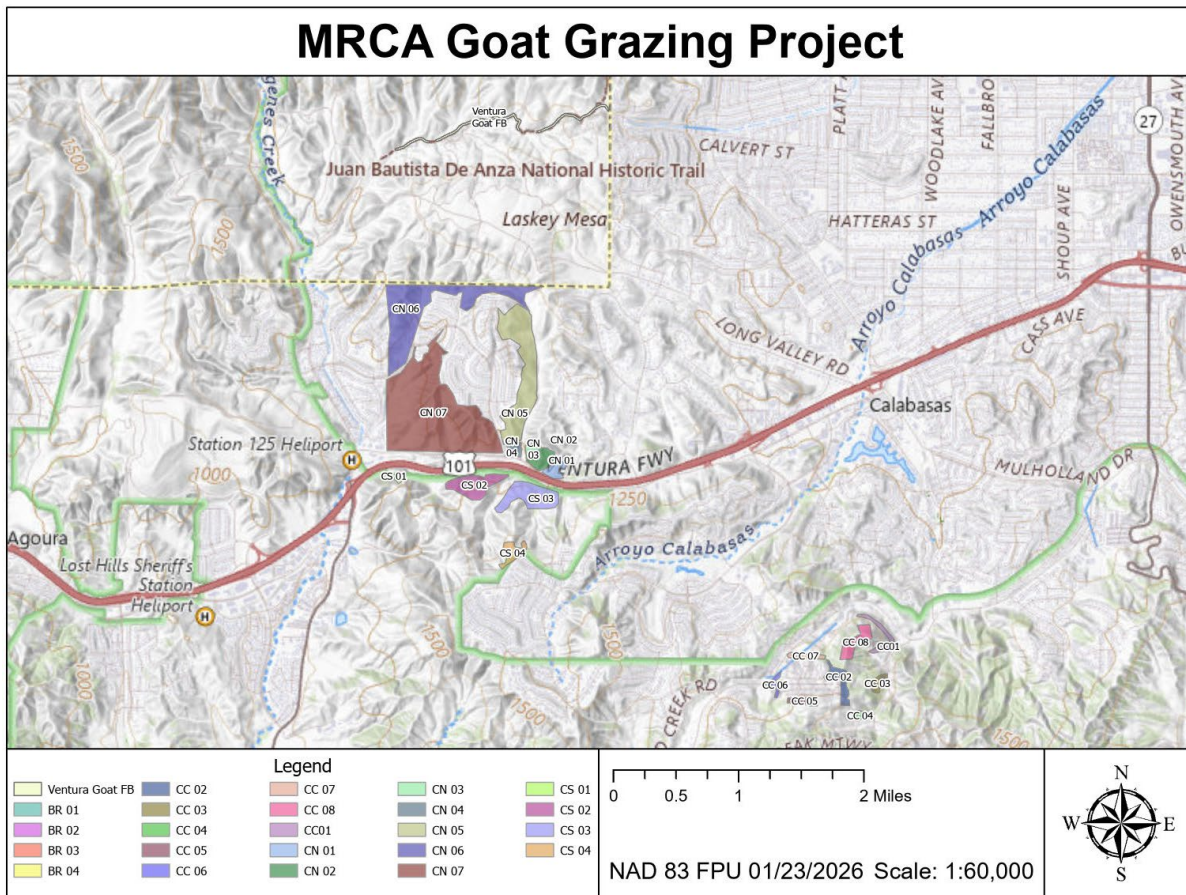



## Weekly Progress Report

5-11-2026 – 5-15-2026

Work Location: (Ventura County)

APN: N/A

Overview: No current operations scheduled. Ongoing planning continues for next stage of the project. Work is estimated to resume on 5/21/2026 with grazing operations.

# Rancho Project

Orthomosaic

05/01/2026

- Grazing  
3,652 ft | 14.3 ac
- Brushing Thinning / Manual  
9,041 ft | 20.9 ac
- Road Side Brushing / Manual  
1,917 ft | 1.1 ac
- Mastication  
3,854 ft | 2.2 ac
- Intermittent Stream (50ft Wide)  
3,441 ft | 1.9 ac
- MRCA Property Line

